

G150

INSTALLATION SITE PREPARATION CHECKLIST

GAGGIA
MILANO

GENERAL MACHINE ENVIRONMENT


- ☐ The installation area is clean and clear of dust and tools. It is not located in an active construction zone.
- ☐ The counter accommodates the machine size and weight:
 - Dimensions: 14.5" (W) x 31" (H) x 23.1" (D)
 - Dimensions with NSF/ANSI 4 legs: 14.5 (W) x 33.6 (H) x 23.1" (D)
 - Weight: 104 lb
- ☐ An access hole has been pre-drilled in the counter for drainage and power in accordance with model installation template
- ☐ Hole in counter is fitted with a collar to protect electrical cord, water line & drain tube.
- ☐ Machine can safely be installed with a minimum clearance of 1 5/8" from the back wall.

ELECTRICAL REQUIREMENTS

G150 Specifications

120/240 V, 60 Hz, 3690 W
NEMA L14-30 Plug

- ☐ Power outlet receptacle is NEMA L14-30R.
- ☐ Dedicated electrical circuit meets the G150 power requirements.
- ☐ No extension cord or power strip on the circuit.

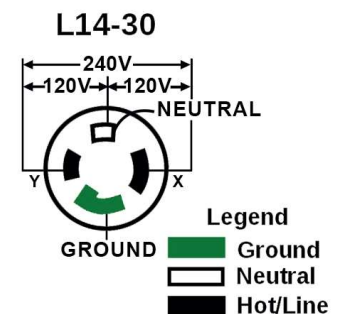

WATER REQUIREMENTS

Pressure & Hardness

- ☐ Pressure is between 21.7 PSI and 123.28 PSI.
- ☐ pH range is between 6.5 and 7.5.
- ☐ Hardness (TDS) is between 89 PPM and 142 PPM.

MANDATORY – Machine water line must be equipped with a water filtration system with softness/filtration capabilities and a descaling device.

Water Network

- ☐ The water network provides cold, drinkable tap water.
- ☐ Dedicated 3/8" diameter water line.
- ☐ Shutoff valve with a 3/8" compression fitting on machine's end.



GAGGIA
MILANO

Evoca North America
2355, avenue Dalton, Québec (Québec) G1P 3S3, Canada
T: 800-561-6162 - F: 800-463-2739
www.evocagroupna.com

Evoca Group Headquarters
Via Roma, 24, 24030 Valbrembo BG Italy
T: +39 035606111 - F: +39 095606560
www.evocagroup.com

G150 | 2024-11



G150

INSTALLATION SITE COMPLIANCE DECLARATION

SITE INFORMATION

Address: _____

Business Name: _____ Contact Phone Number: _____

Contact Name: _____ Contact Email: _____

UNIT INFORMATION

Machine Model: _____ Required Installation Date: _____

I hereby confirm that:

- _____ (initials) The installation site is compliant with all the requirements listed in the Site Preparation Check-List I received.
- _____ (initials) The site is ready for the installation to be scheduled with an Evoca North America certified technician.
- _____ (initials) I will have on site all the products required (coffee beans and soluble products) for the installation technician to fill and test the unit.
- _____ (initials) A water filtration system with softness/filtration capabilities and a descaling device will be installed on the water line prior to the visit of the installation technician.

Please sign and send this form completed to Webstaurant at dropshipmentsupport@webstaurantstore.com, along with photos of the following items:

- ☐ Counter Top ☐ Water Drain
☐ Plug Outlet

Please allow a minimum of 10 business days for order processing/installation scheduling

Signature: _____ Date: _____

Agreement

I sign and send this form completed to Webstaurant as a confirmation that the installation site is compliant with the requirements of the model listed above. This is the official request to schedule the installation with an Evoca North America certified technician.

I acknowledge that my company will be charged if a second installation visit is required in the event that the installation site is not compliant with all the Site Preparation Check-List requirements.

I acknowledge that non-compliance with any of the elements listed in the Site Preparation Check-List will affect the warranty coverage of the machine.
